NUMMER ETT BUILDERS AND TRADING
GENERAL BUILDING CONSTRUCTION RENTAL SERVICE AND TRADING
153 LIBYA EXT. GREENHEIGHTS SUBD. PH.6 NANGKA, MARIKINA CITY
email: nummerettbuilders_trading@yahoo.com
Telephone no.: 8255-8327

MATERIAL REQUEST FORM

Project Name:	MARINA SKYLINE RESIDENCES - TOWER B	**M.R.F.No.:**	MRF-372
Location:	1045 EDSA, BRGY. 143, PASAY CITY, METRO MANILA	**Request Date:**	October 2, 2026

ITEM NO.	QTY	UNIT	DESCRIPTION	DATE NEEDED	PURPOSE	LOCATION	REMARKS
1	12	PCS	TEMPERED GLASS PANEL 10MM CLEAR, 900 X 2100MM	10/30/2026	3RD FLOOR GLASS DOOR AND PARTITION WORKS PER KEY PLAN CP-04.	3RD FLOOR STAGING AREA	
2	18	PCS	TEMPERED GLASS PANEL 10MM CLEAR, 800 X 2100MM	10/30/2026	3RD FLOOR GLASS DOOR AND PARTITION	3RD FLOOR	
					WORKS PER KEY PLAN CP-04.	STAGING AREA	
3	12	SET	FRAMELESS GLASS DOOR HARDWARE SET, TOP-HUNG,	10/30/2026	3RD FLOOR GLASS DOOR AND PARTITION	3RD FLOOR	
			STAINLESS		WORKS PER KEY PLAN CP-04.	STAGING AREA	
4	30	PCS	STAINLESS STEEL DOOR PULL HANDLE 1000MM, 32MM TUBE,	10/30/2026	3RD FLOOR GLASS DOOR AND PARTITION	3RD FLOOR	
			BRUSHED		WORKS PER KEY PLAN CP-04.	STAGING AREA	
5	14	PCS	FRAMELESS SHOWER PARTITION PANEL 8MM TEMPERED, H	10/30/2026	3RD FLOOR GLASS DOOR AND PARTITION	3RD FLOOR	CONFIRM TEMPERED
			2000MM		WORKS PER KEY PLAN CP-04.	STAGING AREA	CERTIFICATE ON
							DELIVERY.
6	24	CARTRIDGE	SILICONE SEALANT, NEUTRAL CURE, CLEAR, 300ML TUBE	10/30/2026	3RD FLOOR GLASS DOOR AND PARTITION	3RD FLOOR	
					WORKS PER KEY PLAN CP-04.	STAGING AREA	
7	60	PCS	GLASS CLAMP, POLISHED STAINLESS STEEL, 4-HOLE 50 X	10/30/2026	3RD FLOOR GLASS DOOR AND PARTITION	3RD FLOOR	
			50MM		WORKS PER KEY PLAN CP-04.	STAGING AREA	
8	4	ROLL	ANTI-BREAK SAFETY FILM 0.4MM, 1220MM WIDE ROLL	10/30/2026	3RD FLOOR GLASS DOOR AND PARTITION	3RD FLOOR	
					WORKS PER KEY PLAN CP-04.	STAGING AREA	
Comments/Special Instructions			SUPPLY PER APPROVED KEY PLAN. DELIVER IN ONE LOT. SITE PERSONNEL INSPECTS ON ARRIVAL.				
Attachments:			MRF 372 - Material Request and Key Plan.pdf				

REQUESTED BY	APPROVED BY	PURCHASER / PROCUREMENT OFFICER	FINANCE OFFICER
ARRIANE AYA M. BAYLON	ENGR. PAOLO REYES	MARIA L. SANTIAGO	RAFAEL LIM


NUMMER ETT BUILDERS AND TRADING

KEY PLAN - 3RD FLOOR, EAST WING - GLASS DOORS AND PARTITION PANELS

PROJECT: MARINA SKYLINE RESIDENCES - TOWER B

SHEET CP-04 SCALE 1:100 DATE OCTOBER 2, 2026 DRAWN ARRIANE AYA M. BAYLON

PLAN

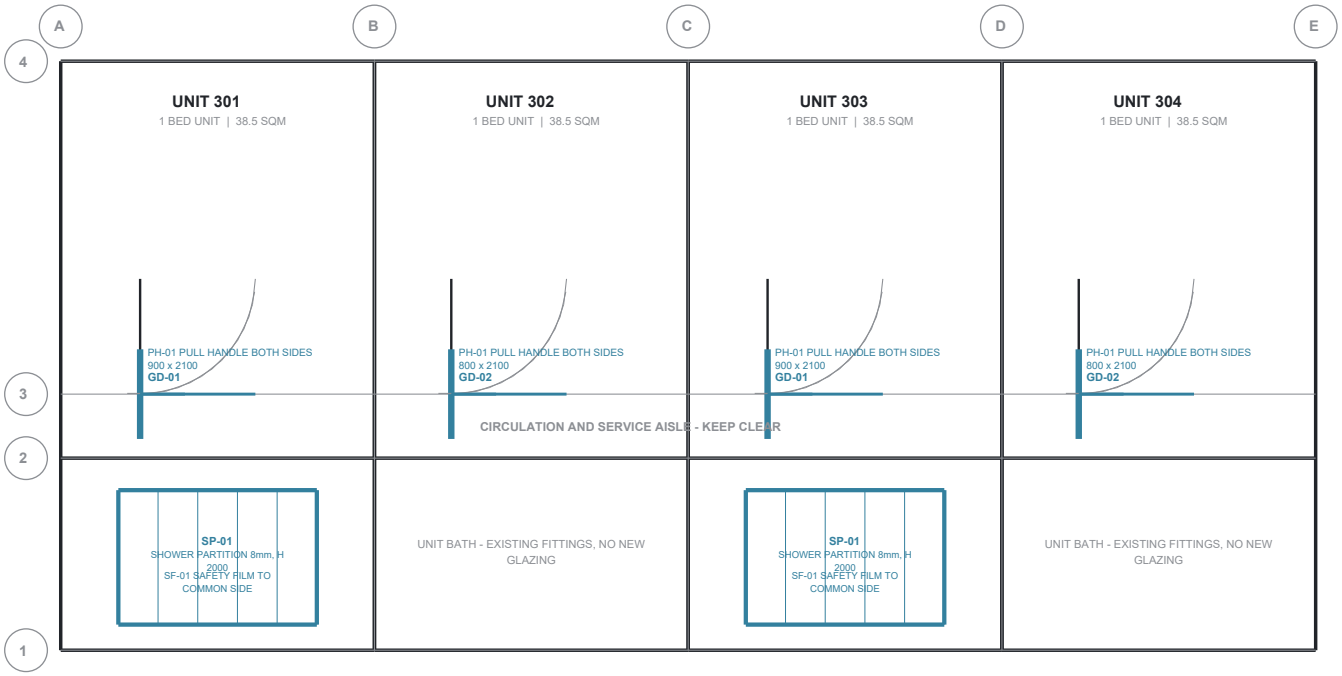

N

LEGEND

GD-01	FRAMELESS GLASS DOOR, TOP-HUNG, 900 x 2100mm, CLEAR 10mm TEMPERED
GD-02	FRAMELESS GLASS DOOR, TOP-HUNG, 800 x 2100mm, CLEAR 10mm TEMPERED
SP-01	FRAMELESS SHOWER PARTITION PANEL, 8mm TEMPERED, H 2000mm
PH-01	STAINLESS STEEL PULL HANDLE 1000mm, 32mm TUBE, BOTH SIDES
SF-01	ANTI-BREAK SAFETY FILM 0.4mm ON GLAZING ADJACENT TO COMMON AREAS
ST-01	NEUTRAL-CURE SILICONE SEALANT, CLEAR, ALL GLASS EDGES

GENERAL NOTES

1. ALL DIMENSIONS ARE IN MILLIMETRES UNLESS NOTED OTHERWISE.
2. DOOR AND PARTITION OPENING SIZES ARE NOMINAL; CONFIRM ON SITE BEFORE ORDER.
3. ALL GLAZING SHALL BE CERTIFIED TEMPERED SAFETY GLASS TO ASTM C1048.
4. TOP-HUNG HARDWARE SHALL BE FULL-HEIGHT 304 STAINLESS STEEL, 100kg RATED.
5. SEAL ALL GLASS EDGES WITH NEUTRAL-CURE SILICONE AFTER INSTALLATION.
6. APPLY SAFETY FILM TO ALL GLAZING ADJACENT TO COMMON AREAS.
7. UNLOADING OF VERTICAL CRATES IS BY THE BUYER.

PREPARED BY

ARRIANE AYA M. BAYLON - SITE PERSONNEL

VERIFIED BY

ENGR. PAOLO REYES

MARINA SKYLINE RESIDENCES - TOWER B	
3RD FLOOR, EAST WING	REV. 01
CP-04	OCT 02, 2026

NUMMER ETT BUILDERS AND TRADING

GENERAL BUILDING CONSTRUCTION RENTAL, SERVICE AND TRADING
93 LIBTAL ST. GREENHILLS SUBO PULO PINAMAMAQUE CITY

SCOPE OF WORK AND MATERIAL SPECIFICATION

CP-04 / MS-03

1. PROJECT

MARINA SKYLINE RESIDENCES - TOWER B, 1045 EDSA, BRGY. 143, PASAY CITY, METRO MANILA. This scope covers the 3rd floor east wing only, comprising units 301 to 304 as shown on key plan CP-04.

2. WORKSCOPE

Supply and install frameless glass doors, glass door hardware, stainless steel pull handles and frameless shower partitions at the 3rd floor east wing, including silicone sealing of all glass edges and application of anti-break safety film to glazing adjacent to common areas.

3. SPECIFICATIONS

All glass panels shall be 10mm thick clear tempered safety glass conforming to ASTM C1048, with safety certification labels on every panel. Shower partitions shall be 8mm thick clear tempered glass at 2000mm height. Doors shall be top-hung on full stainless steel hardware sets rated for 100kg. Pull handles shall be 1000mm brushed stainless steel with 32mm tube. All stainless fittings shall be 304 grade.

4. INSTALLATION

Installation shall be by an approved frameless glass door installer. Confirm all opening sizes on site before releasing the order to the supplier. Unloading of vertical crates is by the buyer. Site Personnel shall inspect and accept all materials on delivery against this material request.

5. DELIVERY

Deliver in one lot to the 3rd floor staging area. Required on site by October 30, 2026. Supplier shall provide certified tempered glass documentation with the delivery.

6. EXCLUSIONS

This scope excludes framing and rough opening preparation, electrical and lighting work, signage, and any work outside the 3rd floor east wing.

7. MATERIAL SCHEDULE

ITEM	DESCRIPTION	QTY	UNIT	REQUIRED ON SITE
1	TEMPERED GLASS PANEL 10mm CLEAR, 900 x 2100mm	12	PCS	30 OCT 2026
2	TEMPERED GLASS PANEL 10mm CLEAR, 800 x 2100mm	18	PCS	30 OCT 2026
3	FRAMELESS GLASS DOOR HARDWARE SET, TOP-HUNG, STAINLESS	12	SET	30 OCT 2026
4	STAINLESS STEEL DOOR PULL HANDLE 1000mm, 32mm TUBE, BRUSHED	30	PCS	30 OCT 2026
5	FRAMELESS SHOWER PARTITION PANEL 8mm TEMPERED, H 2000mm	14	PCS	30 OCT 2026
6	SILICONE SEALANT, NEUTRAL CURE, CLEAR, 300ml TUBE	24	CARTRIDGE	30 OCT 2026
7	GLASS CLAMP, POLISHED STAINLESS STEEL, 4-HOLE 50 x 50mm	60	PCS	30 OCT 2026
8	ANTI-BREAK SAFETY FILM 0.4mm, 1220mm WIDE ROLL	4	ROLL	30 OCT 2026

8. REFERENCES

Material Request Form MRF-372 dated October 2, 2026.
Key plan CP-04, 3rd floor east wing, revision 01.
This specification and the approved key plan together define the requested materials. Any material not listed here is outside this request.

ARRIANE AYA M. BAYLON - SITE PERSONNEL

ENGR. PAOLO REYES - APPROVING ENGINEER
